




**MOODY METHODIST CHURCH**  
**2021 MOODY STEEPLE CLADDING REPAIRS**  
**WEEKLY FIELD REPORT No. 04**  
**WEEK OF 2/08/2021**

**Weekly Weather**

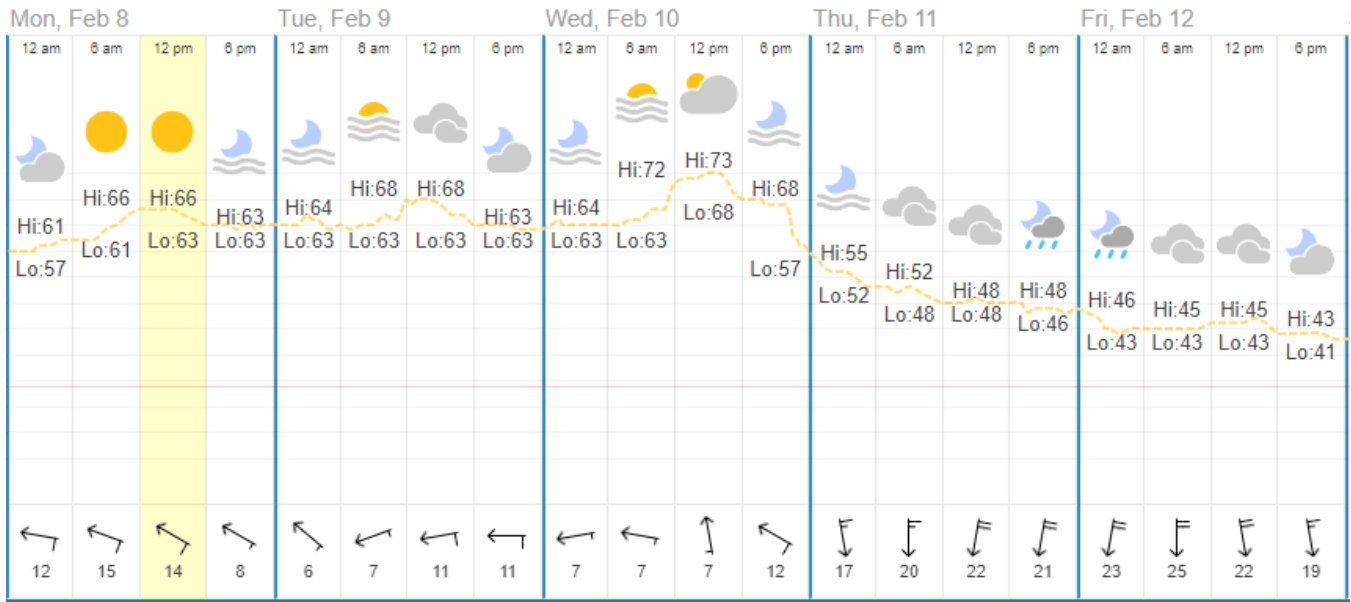

**Date: Monday, February 08, 2021**

**On Site:** Coltzer Company, LLC  
 RB Hash  
**Temperature – Low/High (°F):** 57/66  
**Rain (Total Inches):** 0.00”  
**Max Wind Speed(mph):** 15 ESE

**Field Note:** **Comments & Photographs:**  
**02 08-01** *Coltzer Company, LLC* on site to observe steeple repairs progress.  
**02 08-02** *RB Hash* continues removing old copper cladding from next tier of the steeple. RB Hash also continues applying waterproofing membrane on the steeple. **(See photo01-04)**





Photo01: Overview of Work in Progress



Photo02: Removed Copper Cladding



Photo03: Exposed Wood Underneath Copper Cladding



Photo04: Waterproof Membrane Applied on Next Tier

Date: Tuesday, February 09, 2021

On Site: Coltzer Company, LLC  
RB Hash

Temperature – Low/High (°F): 63/68

Rain (Total Inches): 0.00

Max Wind Speed(mph): 10 NE

Field Note: Comments & Photographs:

02 09-01 **Coltzer Company, LLC** on site to observe steeple repairs progress.

02 09-02 **RB Hash** continues removing copper cladding on the next tier of the steeple. (see photo05-07)



Photo05: Steel Beams Beneath the Copper Cladding



Photo06: More Copper is Removed



Photo07: Overview of Work in Progress

Date: Wednesday, February 10, 2021

On Site: Coltzer Company, LLC  
RB Hash

Temperature – Low/High (°F): 54/64

Rain (Total Inches): 0.00

Max Wind Speed(mph): 16 SE

Field Note: Comments & Photographs:

02 10-01 *Coltzer Company, LLC* on site to observe steeple repairs progress.

02 10-02 *RB Hash* continues removing copper cladding from the upper tier of the steeple. (see photo08-09)





Photo08: Overview of Work in Progress



Photo09: Copper Cladding Removed from Upper Level of Steeple

**Date: Thursday, February 11, 2021**

<b>On Site:</b>	N/A	<b>Temperature – Low/High (°F):</b>	46/55
		<b>Rain (Total Inches):</b>	0.20"
		<b>Max Wind Speed(mph):</b>	22 N

**Field Note:**      **Comments & Photographs:**  
02 11-01      *Coltzer Company, LLC* was not on site due to rain and heavy winds.

**Date: Friday, February 12, 2021**

<b>On Site:</b>	N/A	<b>Temperature – Low/High (°F):</b>	41/46
		<b>Rain (Total Inches):</b>	0.56"
		<b>Max Wind Speed(mph):</b>	25 N

**Field Note:**      **Comments & Photographs:**  
02 12-01      *Coltzer Company, LLC* was not on site due to rain and heavy winds.

**DISTRIBUTION LIST**

NAME	REPRESENTING	PHONE NUMBER	E-MAIL
Bill Coltzer	Coltzer Company, LLC	409-740-0090	bcoltzer@z6consulting.com
Lidija Bikova	Zero/Six Consulting, LLC	409-740-0090	LBikova@z6consulting.com
Richard Parks	Coltzer Company, LLC	470-314-2821	<a href="mailto:rparks@z6consulting.com">rparks@z6consulting.com</a>
Sam Caminade	Moody Church	409-771-7785	sam@moody.com
Bryan Hash	R.B. Hash Roofing		rbh@rbhash.com
John Garza	R.B. Hash Roofing		jgarza@rbhash.com
Justin Wenner	Betco Scaffolding		<a href="mailto:justin.wenner@scaffold.com">justin.wenner@scaffold.com</a>
Steve Grimes	Betco Scaffolding		<a href="mailto:steve.grimes@scaffold.com">steve.grimes@scaffold.com</a>

*The preceding represents Coltzer Company's understanding of the principal matters discussed and/or observed. Written comments with regard to the content of this report should be received by Coltzer Co. within three days from date of issue. After that date, these notes shall stand as a final accounting of the items discussed and/or observed.*

